



# APM Buildings Quotation Package



**QUOTATION FOR:**  
With Attic Attic406012

**CONTACT:**  
1-888-261-2488

**CONSTRUCTION:** Post Frame  
**DIMENSIONS:** 40' X 60' X 12'

**SPECIFICATIONS FOR 40' X 60' X 12' POST FRAME PACKAGE:**

• **MATERIAL PACKAGE**

- Pre-Engineered Wood Trusses (6.5/12 Pitch, 2' O/C)
- 4.5 x 5.25 APM Stock Columns 3 Ply Eave Posts (8' O/C)
- 4.5 x 5.25 APM Stock Columns 3 Ply Gable Posts (10' O/C)
- 2 x 8 Treated Skirt Boards (1 Row)
- 2 x 4 Wall Girts (24" O/C) and Roof Purlins (24" O/C)
- 1.75 x 9.5 Double Top Girt Truss Carrier
- Beige Tuff Rib 3 Panel Steel Siding
- Forest Green Tuff Rib 3 Panel Steel Roof
- No Concrete Provided

• **DOORS & WINDOWS**


- Two 10 X 10 Clopay T52S Ins. Std. Trk. w/o Openers
- One 3' 6 Panel Entry Door
- One Stock Windows 3' x 3' 8" Single Hung Window

• **12" EAVE OVRHG., 0" GABLE OVRHG. W/ VENTED STEEL SOFFIT**

• **FASTENERS**

- 1 In.Metal to Wood Screws for Steel Wall, Roof Panels
- 4.5 Headlok Screws for Truss Carrier
- 16D Galv. Nails for Skirt Board
- Galvanized Steel Framing Nails

• **DETAILED BUILDING PLANS**

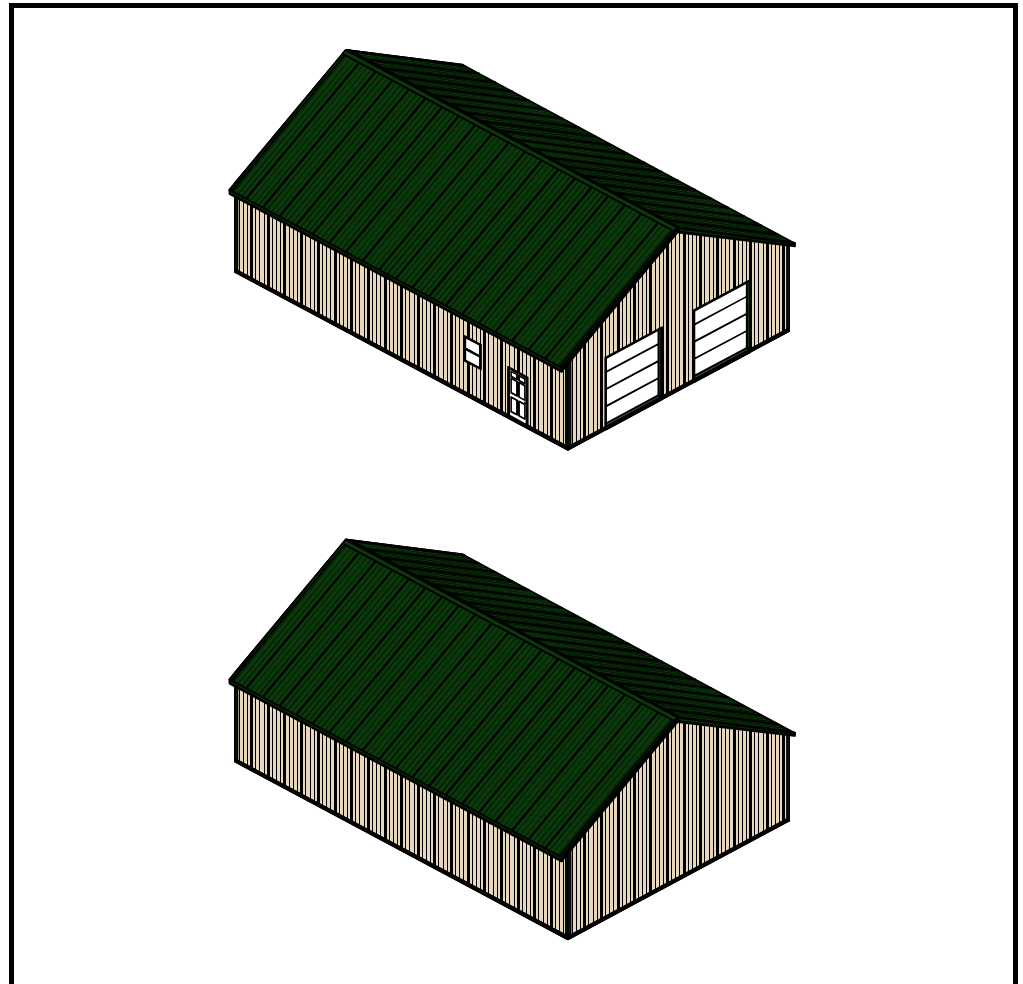

Subtotal	\$22,165.68
Discount	(\$3,103.00)
<b>Total</b>	<b>\$19,062.68</b>

**ESTIMATE NUMBER: 19867**

**Eave 1**

