



APM Buildings Quotation Package



QUOTATION FOR:

With Lean-To Lean243212

CONTACT:

1-888-261-2488

CONSTRUCTION:

Post Frame

DIMENSIONS:

24' X 32' X 12'

EAVE1 PORCH

10' X 32' X 9' 3"

SPECIFICATIONS FOR 24' X 32' X 12' POST FRAME PACKAGE:

• MATERIAL PACKAGE

- Pre-Engineered Wood Trusses (4/12 Pitch, 4' O/C)
- 4.5 x 5.25 APM Stock Columns 3 Ply Eave Posts (8' O/C)
- 4.5 x 5.25 APM Stock Columns 3 Ply Gable Posts (8' O/C)
- 2 x 8 Treated Skirt Boards (1 Row)
- 2 x 4 Wall Girts (24" O/C) and Roof Purlins (24" O/C)
- 2 x 10 Double Top Girt Truss Carrier
- Beige Tuff Rib 3 Panel Steel Siding
- Forest Green Tuff Rib 3 Panel Steel Roof
- No Concrete Provided

• DOORS & WINDOWS

- Two 10 X 10 Clopay T52S Ins. Std. Trk. w/o Openers
- One 3' 6 Panel Entry Door
- One Stock Windows 3' x 3' 8" Single Hung Window


• 10' X 9' 3" X 32' DUAL PITCH PORCH, EAVE 1

• 12" EAVE OVRHG., 0" GABLE OVRHG. W/ VENTED STEEL SOFFIT

• FASTENERS

- 1 In.Metal to Wood Screws for Steel Wall, Roof Panels
- 4.5 Headlok Screws for Truss Carrier
- 16D Galv. Nails for Skirt Board
- Galvanized Steel Framing Nails

• DETAILED BUILDING PLANS

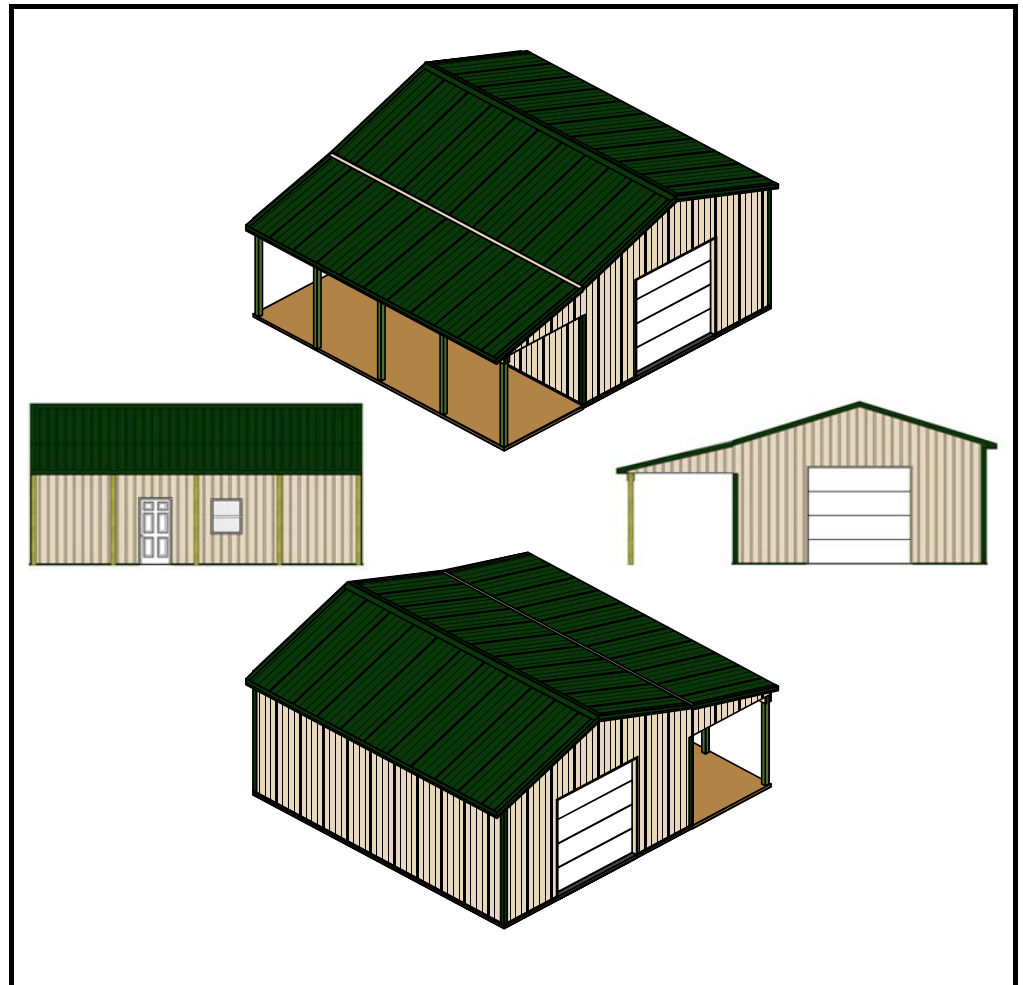

Subtotal	\$10,323.61
Discount	(\$1,238.00)
Total	\$9,085.61

ESTIMATE NUMBER: 19893



POLE LAYOUT

Personal Use, 768 sq. ft.



Eave 1

